



Construction Update

- Construction progressing on schedule
 - Extensive Covid-19 control measures continue
 - Pressure testing of all three boilers complete
 - Stack installed
 - Tipping Hall, Bunker and Boiler Hall steelwork substantially complete.
 - Cladding installation underway
 - Administration building internal fit out ongoing
 - Process steelwork approaching completion.
 - Process equipment installation progressing well
 - Flue Gas Treatment equipment installation works approaching completion
 - Network Rail Level Crossing upgrade complete
 - Site workforce currently around 700 persons per day
 - Almost 1.5 million person hours worked in total to date
-

Aerial Photograph – June 2020

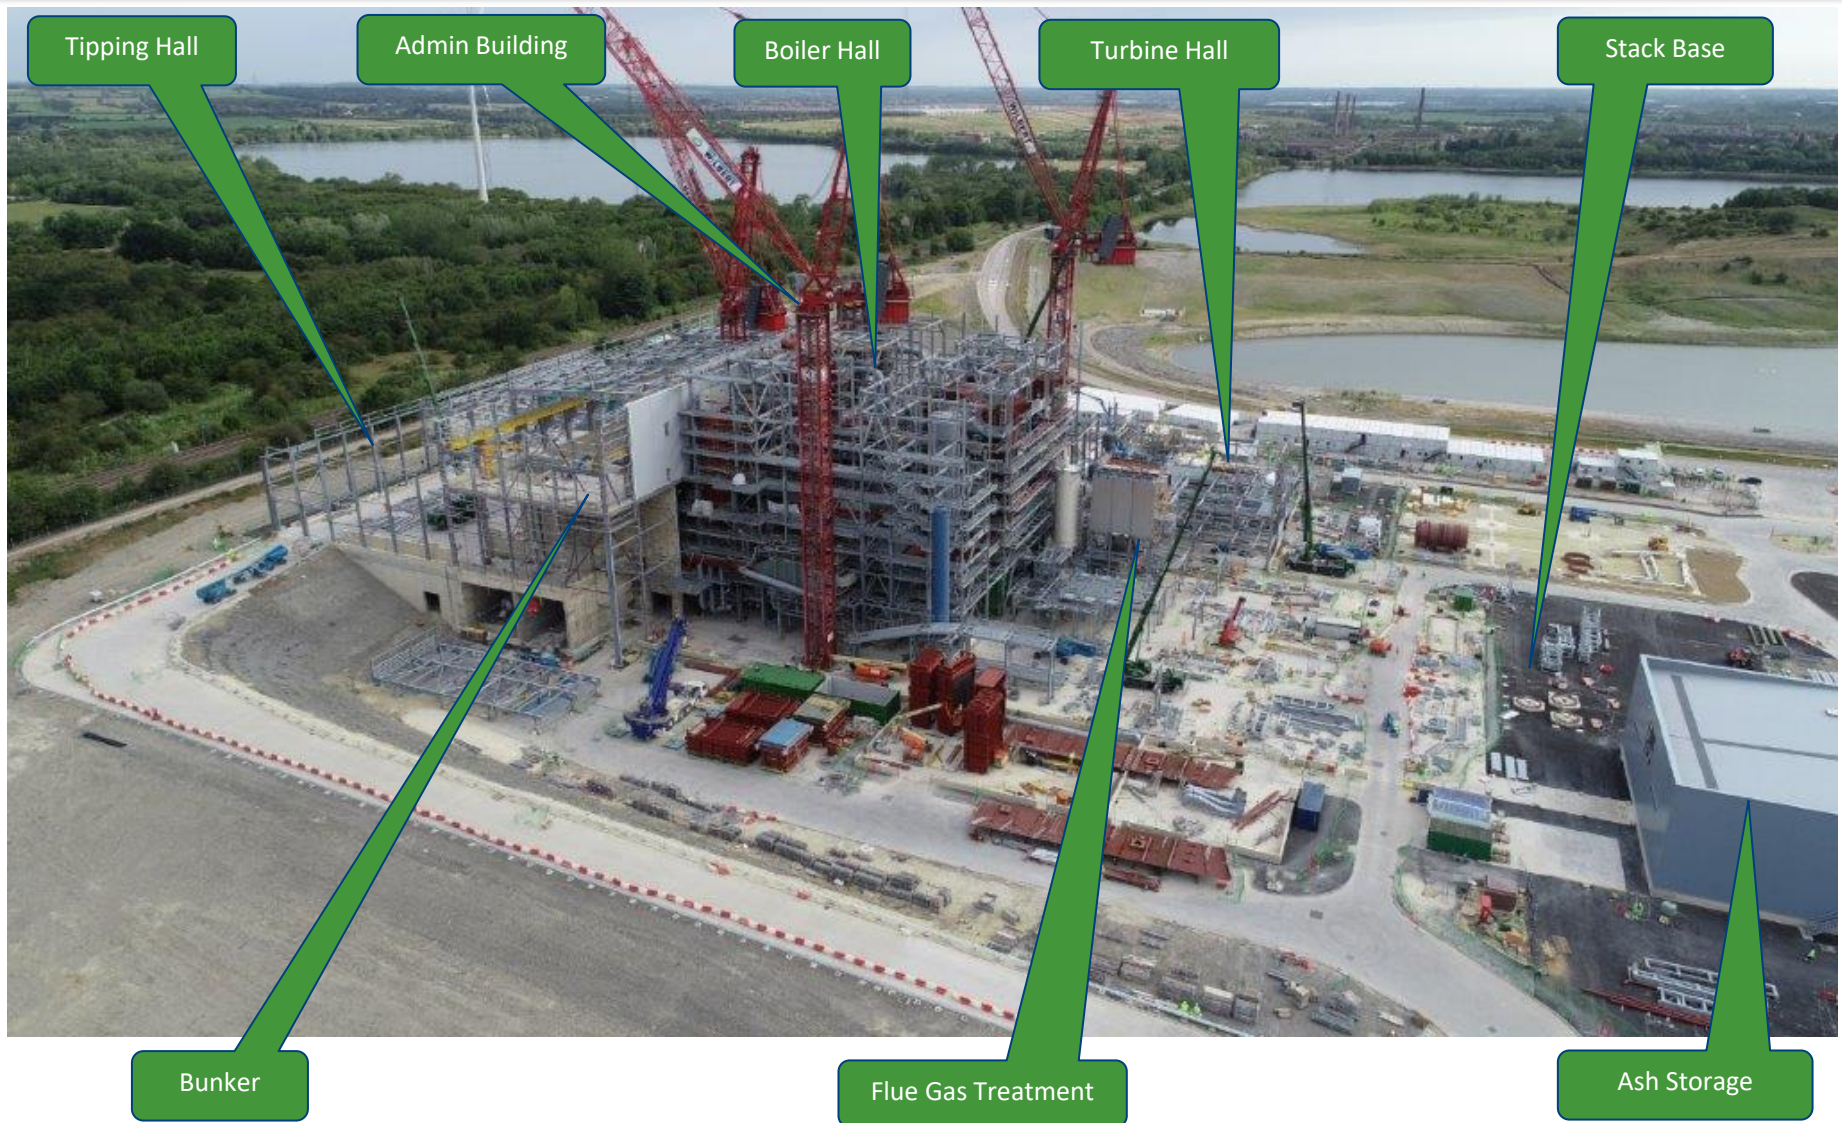

Aerial Photograph – September 2020

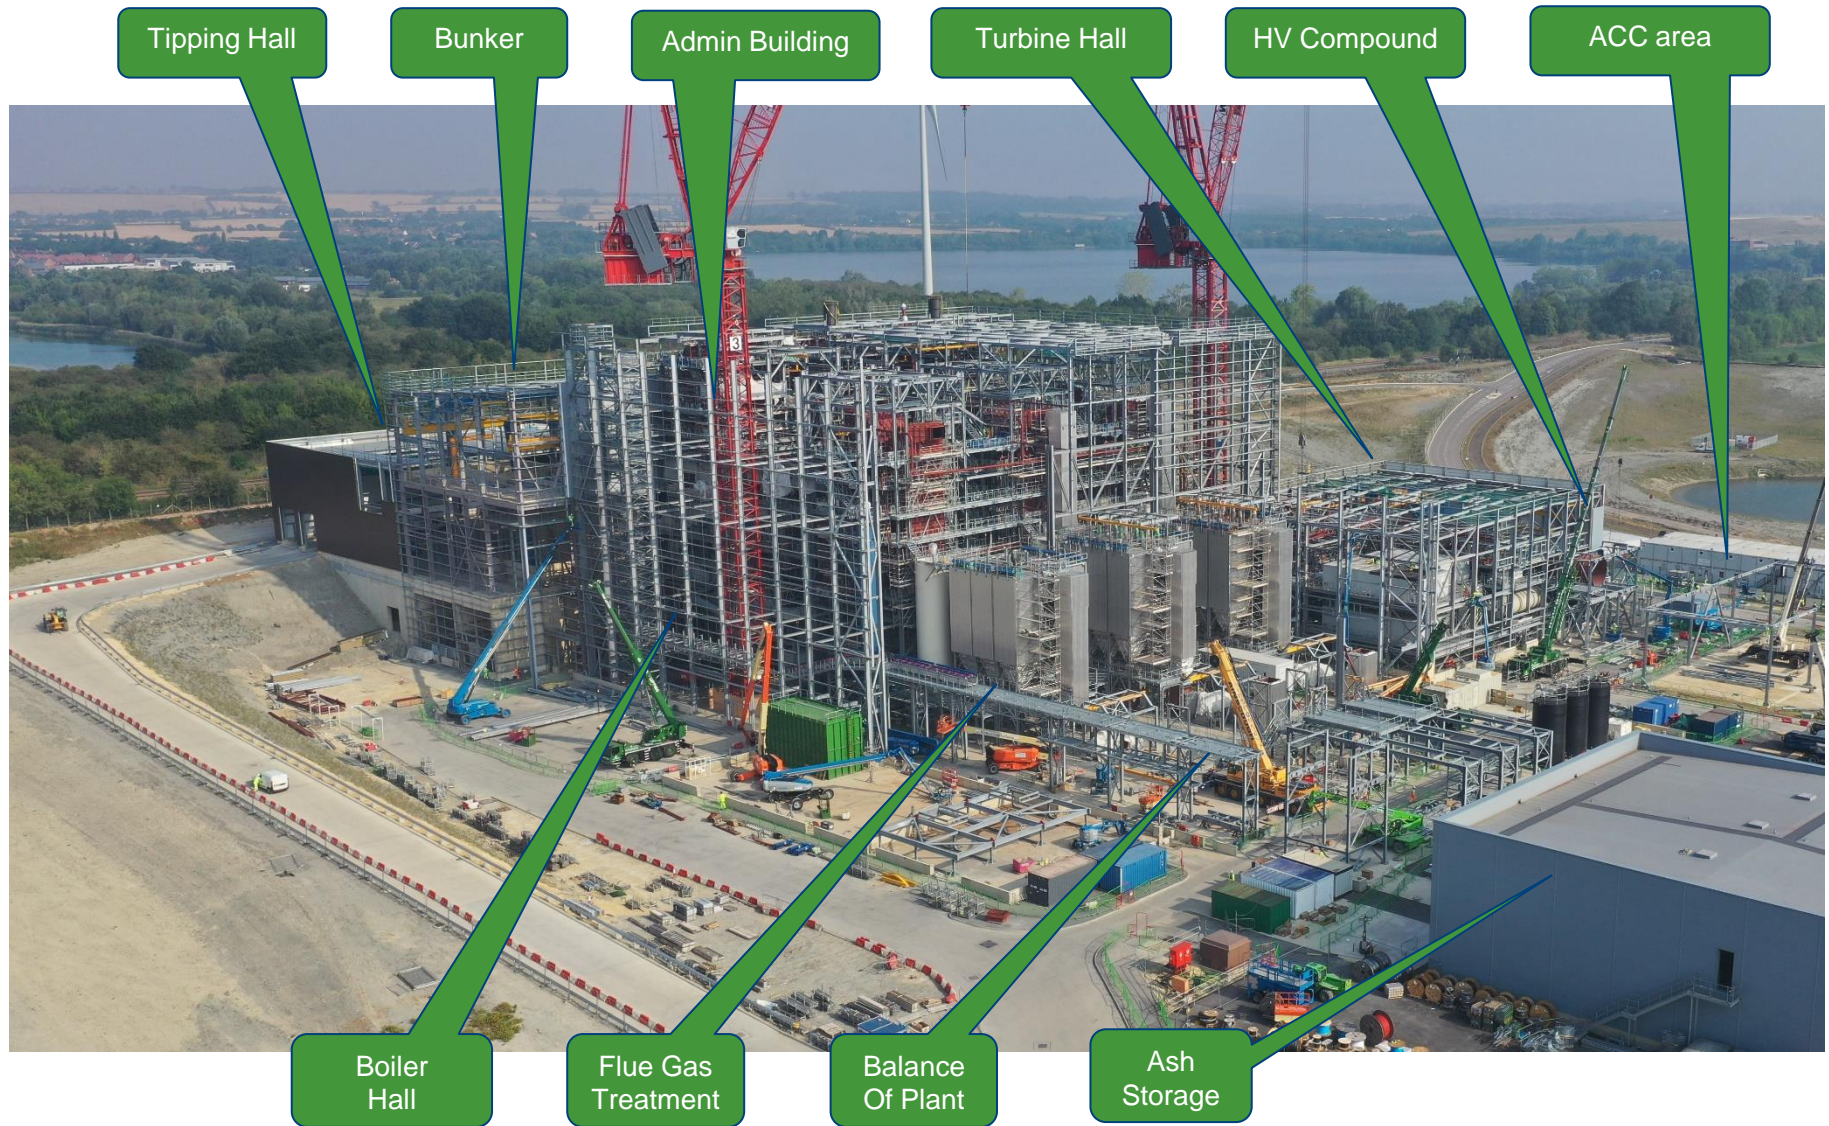

Rookery Progress Photos

Vibrating Conveyor



Stack Erection



Turbine



ACC Erection



Network Rail works complete



Comparison with 3D Model



Deliveries of Abnormal Loads

- Deliveries of Abnormal loads are now complete













Off Site Works

- UKPN HV grid connection works
 - Physical installation works complete.
 - Connection to be energised in September providing additional import capacity
 - Anglian Water
 - Works in Green Lane complete
 - Anglian Water wider main improvement works in Stewartby Village ongoing
 - Network Rail
 - Level crossing upgrade works completed on schedule.
-

Construction – 3 month lookahead

- Energisation of UKPN grid connection
 - Quality control and inspection activities on completed works
 - Removal of tower cranes
 - Completion of structural steel erection
 - Continuation of building cladding installation
 - Completion of process equipment erection
 - Cable pulling and termination
 - Installation of electrical equipment, lighting & HVAC
 - Initial commissioning activities
-

Project Programme

Activity	2018	2019	2020	2021	2022
Works Commencement NTP March 2019					
Access Road & Green Lane Junction					
Civil Construction (incl. piling)					
M&E Installation					
Boiler Pressure Testing					
Cold Commissioning (Power on Sept 2020)					
Hot Commissioning (First waste fire May 2021)					
Testing & Full Operation					

Covid-19 Management & Action Plan

- All arrangements are in line with current UK Government guidance and Site Operating Procedures published by the Construction Leadership Council
 - UK Government position since the start of the pandemic has been that where suitable measures can be implemented, construction sites in England should remain operational
 - The Plan for the Rookery project includes:
 - Transport to site has been re-arranged to ensure that only personnel who are sharing accommodation are travelling together
 - All persons arriving at site are subject to temperature screening
 - Workforce start, finish and break times are staggered to avoid large groups
 - Additional units have been installed in the welfare area (canteen, locker rooms & offices) to provide extra space and enable social distancing
 - Additional handwashing facilities and sanitiser
 - Additional cleaning / disinfection
 - Skilled staff involved in construction of waste management facilities are exempt from 14 day quarantine for arrivals into UK from overseas
-

Temporary Extension of Working Hours - Further Applications

- Development Consent Order states “*Construction work ... may not take place other than between 0700 and 1900 hours on weekdays and 0700 and 1300 hours on Saturdays... unless otherwise agreed in writing by Central Bedfordshire Council.*”
 - Permission has been sought to extend the site working hours to mitigate against time lost due to Covid-19 and to allow workforce to be split across several shifts to enable improved social distancing
 - As reported during the June CLP, permission has been granted to complete Welding Works (Boiler and Process Pipework) between 23 June – 23 December 2020, 24 hours / 7 days per week. This permission remains in place.
 - A further application was submitted to Central Bedfordshire Council on 17th September covering Steel Erection, Process Equipment Installation, Cladding Installation and Deliveries & Offloading
 - 1st October – 31st December 2020 (No external works will be undertaken from 25/12/2020 to 31/12/2020.)
 - Monday to Friday: 1900 – 2200
 - Saturday: 1300 - 1600
 - Sunday: 0700 - 1600
 - Decision pending
-
