



Newhurst ERF Local Liaison Committee Project Update April 2021

Newhurst Energy Recovery Facility

	Newhurst
Location	Leicestershire, England
Capacity (gross)	350 ktpy; ~42 MW
Financial Close	February 11, 2020
Engineer, Procure, Construct (EPC)	Hitachi Zosen INOVA (HZI)
Operator	Covanta
Scheduled Completion Date	Q2 2023



Design (72% complete) and Procurement & Manufacturing (48% complete) progressing on time

Manufacturing of main components, including Turbine and Boiler, progressing on time


Construction (31% complete) progressing on time

Building Steelwork erection has commenced


Civil Works nearing completion ready for handover to Mechanical & Electrical Contractors

Awarded a score of 40/50 by the Considerate Constructors Scheme ('Excellent' in every category)

General Arrangement

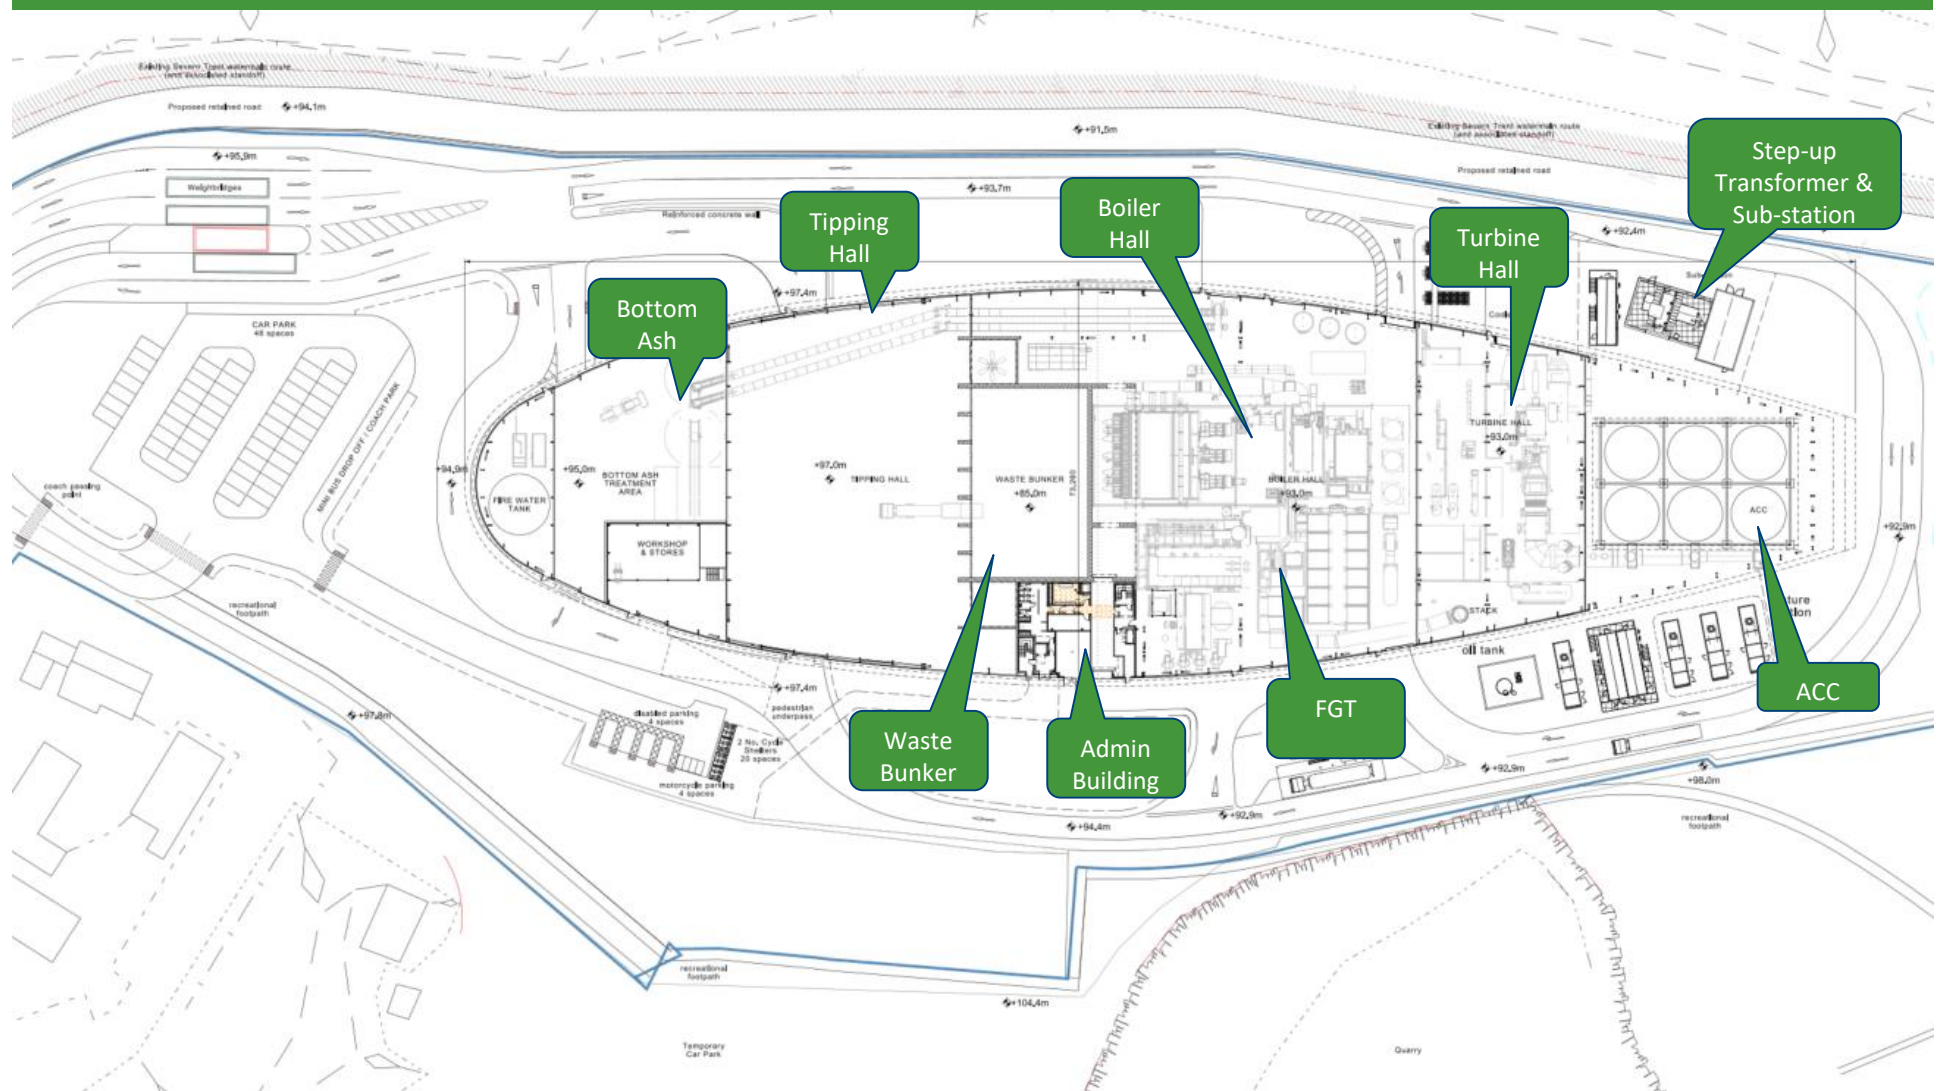

Project Timeline

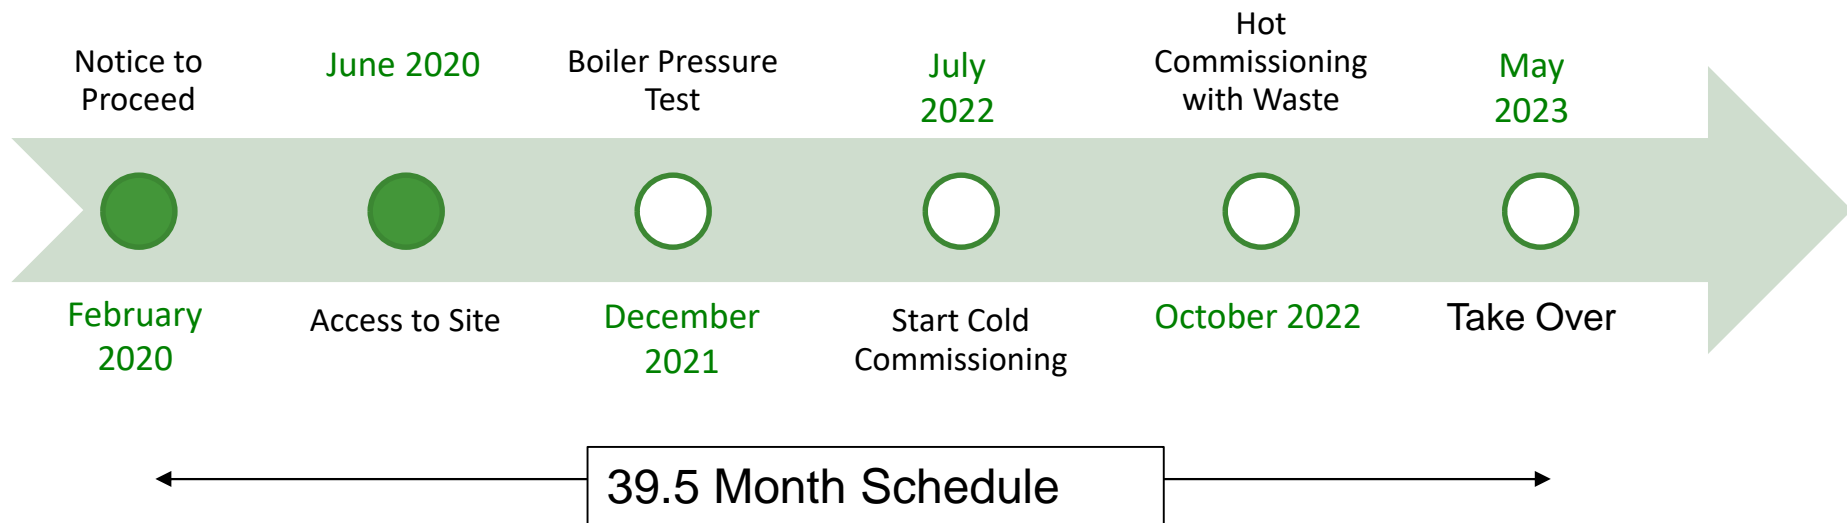

October 2020



January 2021



April 2021



April 2021




Progress Photos



COVID-19 Management & Action Plan

- All arrangements are in line with current UK Government guidance and Site Operating Procedures published by the Construction Leadership Council
- UK Government position since the start of the pandemic has been that where suitable measures can be implemented, construction sites in England should remain operational.
- The Plan for the Newhurst project includes:
 - All persons arriving at site are subject to temperature screening.
 - Workforce start, finish and break times are staggered to avoid large groups.
 - Site Welfare and Offices have been designed to be large enough to enable social distancing.
 - Additional handwashing facilities and sanitiser.
 - Expanded the site cleaning team to ensure areas are cleaned and disinfected frequently.
 - Masks are being worn when moving around offices.
 - Site support staff working from home where possible.
 - Full-time Medic on site with Covid-testing capability, should it be required.
 - 'Misting' tunnels in operation to disinfect clothing.

COVID-19 Site Measures



3 Month Lookahead

- Civil Works package nearing completion.
- Building Steelwork will continue, Building Cladding will commence.
- M&E Contractors will commence on site, beginning with Process Steelwork, then Boiler Erection.
- Factory inspections to check on manufacturing progress (remotely due to Covid-restrictions).
- Non-construction related visits will hopefully be able to commence soon – subject to Government and Construction Leaderships Council advice.
- ***Any questions?***
