


Construction Update – April 2021

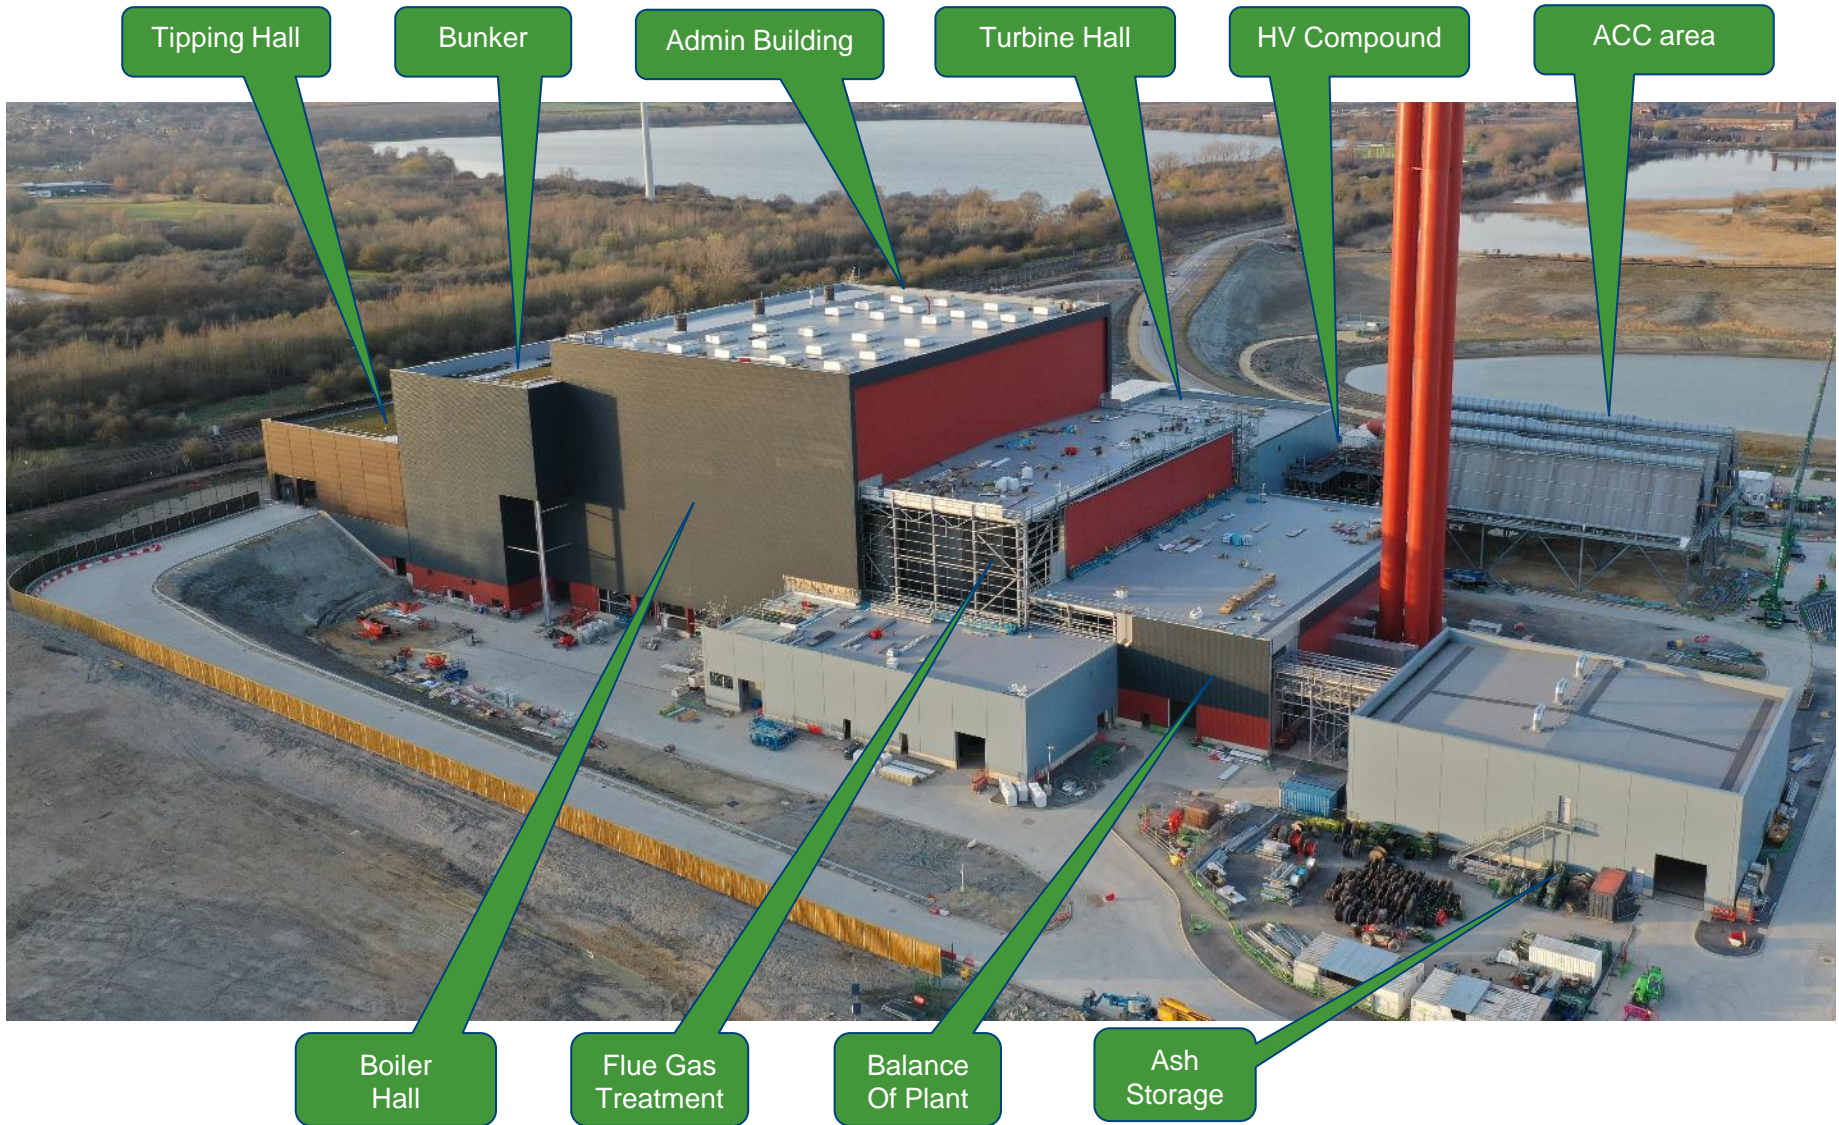

Commissioning Update – April 2021.

- “Cold Commissioning” - January 2021 to May 2021.
 - Functional testing of equipment carried out prior to the introduction of consumables (e.g. fluids & gases) and fuel (diesel, waste),
 - Currently in progress and approaching completion.
 - “Hot Commissioning” - April 2021 to December 2021.
 - Operational testing carried out with the inclusion of consumables (e.g. fluids & gases) and fuel (diesel, waste).
 - First heating of boilers began in early April (known as “Boil-out”).
 - Steam blow activities due to take place in May 2021.
 - *Reminder: Steam blowing can generate some noise. This activity is not permitted overnight.*
 - First waste deliveries expected in May and first waste fire in late May/early June.
-
